

REPORT NO: CRVW S1-3/2024/10

PROJECT PROGRESS REPORT

OCTOBER 2024



DEVELOPER:



SAS e GLUT JV Pvt Ltd

CONTRACTOR:



GLUT Investments
private limited

PROJECT TITLE: MIXED USE RESIDENTIAL COMPLEX AT HULHUMALE (THE CREEK VIEW)
DEVELOPER: SASe GLUT JV PVT. LTD.
CONTRACTOR: GLUT INVESTMENTS PVT. LTD.
LOCATION: LOT NO: S1-3, LOT: 11445 HULHUMALE', MALDIVES

PROJECT BREIF:

The Creek View at Hulhumale Phase-1 is a pristine, spacious condominium project brought to you by the company SASe Glut Joint-venture Private Limited. The development is located at Lot 11445, Kuredhimaa Hingun overseeing the creek separating phase I and phase II of Hulhumale'.

The building comprises 114 apartments with 2 room, 3 room and 4 room units, each carefully designed to ensure the separation of spaces with special attention given to privacy and offer a homely feeling. Each apartment has a mini backyard with access from the kitchen. The kitchens are designed as enclosed spaces separated by masonry and glass partitions.

The apartment units are designed to make the most of natural air and light ventilation with floor to ceiling high windows. These large windows are also placed with an offset from the periphery to prevent direct sun and rain exposure. As many prefer to shape every element of their home environment, carefully choosing their furniture, curtain & paint, we find it best to engage prospective tenants during the interior design process. Those looking to occupy the new home hassle-free have the option to choose from fully fitted, furnished units that come in a different configuration of colour, style & décor.

The access to the residential units is well separated from the commercial area on the ground and the first floor to ensure privacy and safety to tenants. In addition, the entrance lobby is designed with a waiting & meeting area for visitors, limiting visitors' access to apartment floors.

Parking is arranged at the basement, ground and first floor with the basement exclusively for car parking. Amenities such as the pool and playgrounds are at ground level. At the same time, all utility services are located at the service lobby to avoid direct contact with any service team member. A separate service elevator will be allocated for the use of the service team for transporting furniture items and trash bins.

1.0 PROJECT PROGRESS REPORT BREIF

- 1.1 All permits and project documentation requirements are submitted and process accordingly.
- 1.2 Drawings and details are submitted and approved.
- 1.3 All land concern and preparation are addressed in coordinated according to the local government requirements.
- 1.4 All necessary activities and preparation are in progress.

2.0 CURRENT STATUS

2.1 Materials and Equipment's Procurement

2.1.1 Material and Equipment Received

Cement, Sand, Aggregates, Pipes, Blocks, Tiles, SPC, Putty, Paint, Wire, U profile, Ceiling material, Aluminium door and windows, Lift, WPC, Fan, Switches, MCB and Sanitary items

2.2 Time Extension has been granted by HDC up to 31st JULY 2025

2.3 Project Progress Meeting by Urbanco

2.3.1 28th Oct 24.

2.4 Site Coordination Meeting with Consultants

2.4.1 Date: 2nd Oct 24, 20th Oct 24.

2.5 Site Coordination Meeting with Sase – Glut

2.5.1 Date: 8th Oct 24, 17th Oct 24, 22nd Oct 24, 24th Oct 24.

2.6 Issue for Construction Drawing

2.6.1 Detail drawings

2.6.1.1 Landscaping, Boundary wall, swimming pool Drawings – Are Pending

2.6.2 Architectural drawings

2.6.2.1 Architectural Floor Plans – Partial Received


2.6.3 Electrical drawings

2.6.3.1 Electrical Floor Plans – Partial Received

2.6.4 Plumbing drawings

2.6.4.1 Plumbing Floor Plans – Partial Received

2.7 Project Status

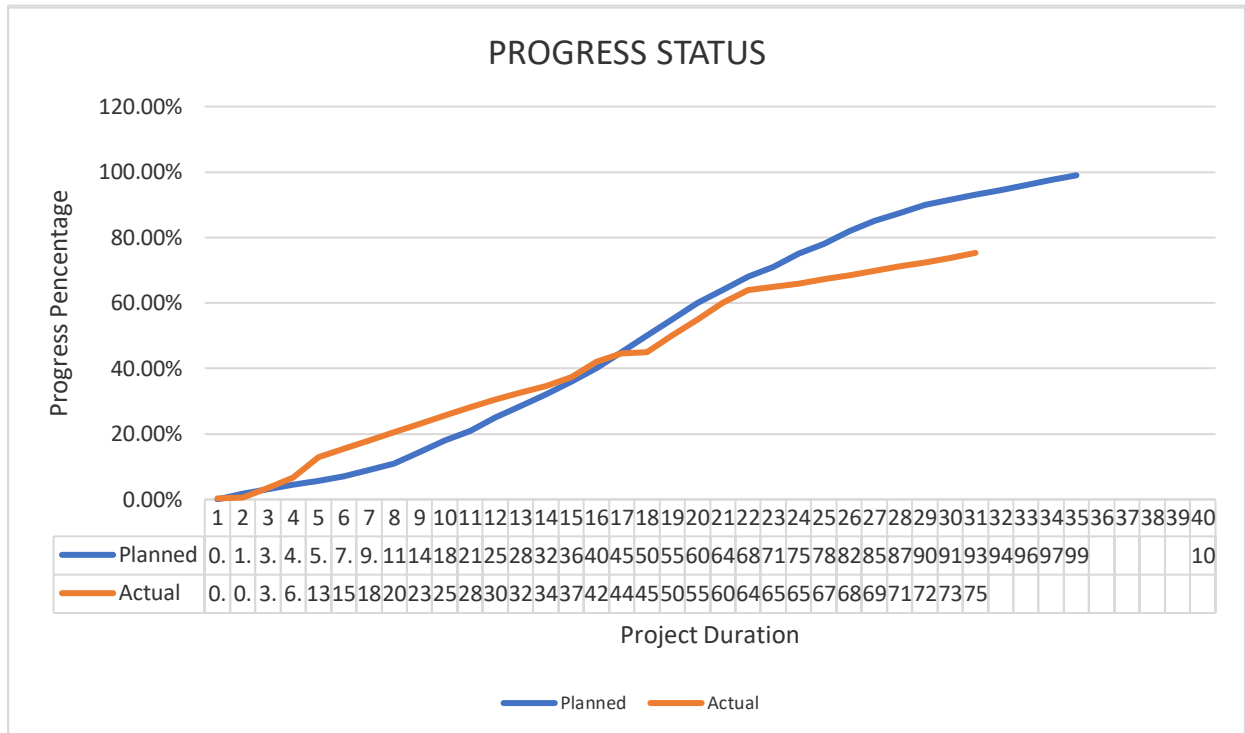

3.0 ONGOING/COMPLETED WORKS

- 3.1 13th floor K,L,M,N block work completed and plastering 75% completed.
- 3.2 2nd and 3rd floor primer and emulsion painting work continuous.
- 3.3 Elevation E2 H and I air well area external plastering completed.
- 3.4 Tile work completed 2nd to 10th floor completed 11th floor continuous.
- 3.5 False ceiling work continuous 2nd to 12th floor common area continuous.
- 3.6 2nd to 8th floor screeding work continuous.
- 3.7 Safety net installation and scaffolding for all round area.
- 3.8 Fresh water line up to 11th floor and common area 9th floor complete.
- 3.9 Floor wiring 11th floor continuous,Ceiling wiring 12th floor continuous.

4.0 UPCOMING WORKS FOR NEXT MONTH

- 4.1 External plastering will complete 2nd to roof terrace.
- 4.2 External putty and painting work will continuous.
- 4.3 Screeding work will complete up to 11th floor.
- 4.4 11th and 12th floor toilet floor tile and wall tile work will complete.
- 4.5 Up to 12th floor floor wiring and 12th floor ceiling wiring will complete.
- 4.6 Common area plumbing work up to 12th floor will complete.
- 4.7 All toilet and balcony water proofing up to 12th floor will complete.
- 4.8 Penthouse roofing sheet fixing 100% will complete.
- 4.9 Safety net installation and internal perimeter scaffolding installation

5.0 ACCIDENT REPORT

5.1 No accident was reported

6.0 CHALLENGES FACED DURING CONSTRUCTION / IMPLEMENTATION

6.1 Weather disruption due to heavy wind and rain (see weather chart–9.0)

7.0 INSTRUCTION GIVEN ON SITE

7.1 Minutes of meeting dated: 5th Oct 24, 12th Oct 24, 19th Oct 24, 26th Oct 24.


8.0 DOCUMENTATION OF APPROVED MATERIALS

8.1 Material submittal Report

- 8.1.1 Ceiling mount light for market and price capped apartment.
- 8.1.2 Hanging light for market and price capped apartment.
- 8.1.3 Wall light for market and price capped apartment.
- 8.1.4 Mirror light for market and price capped apartment.

9.0 WEATHER CHART

9.1 OCTOBER 2024

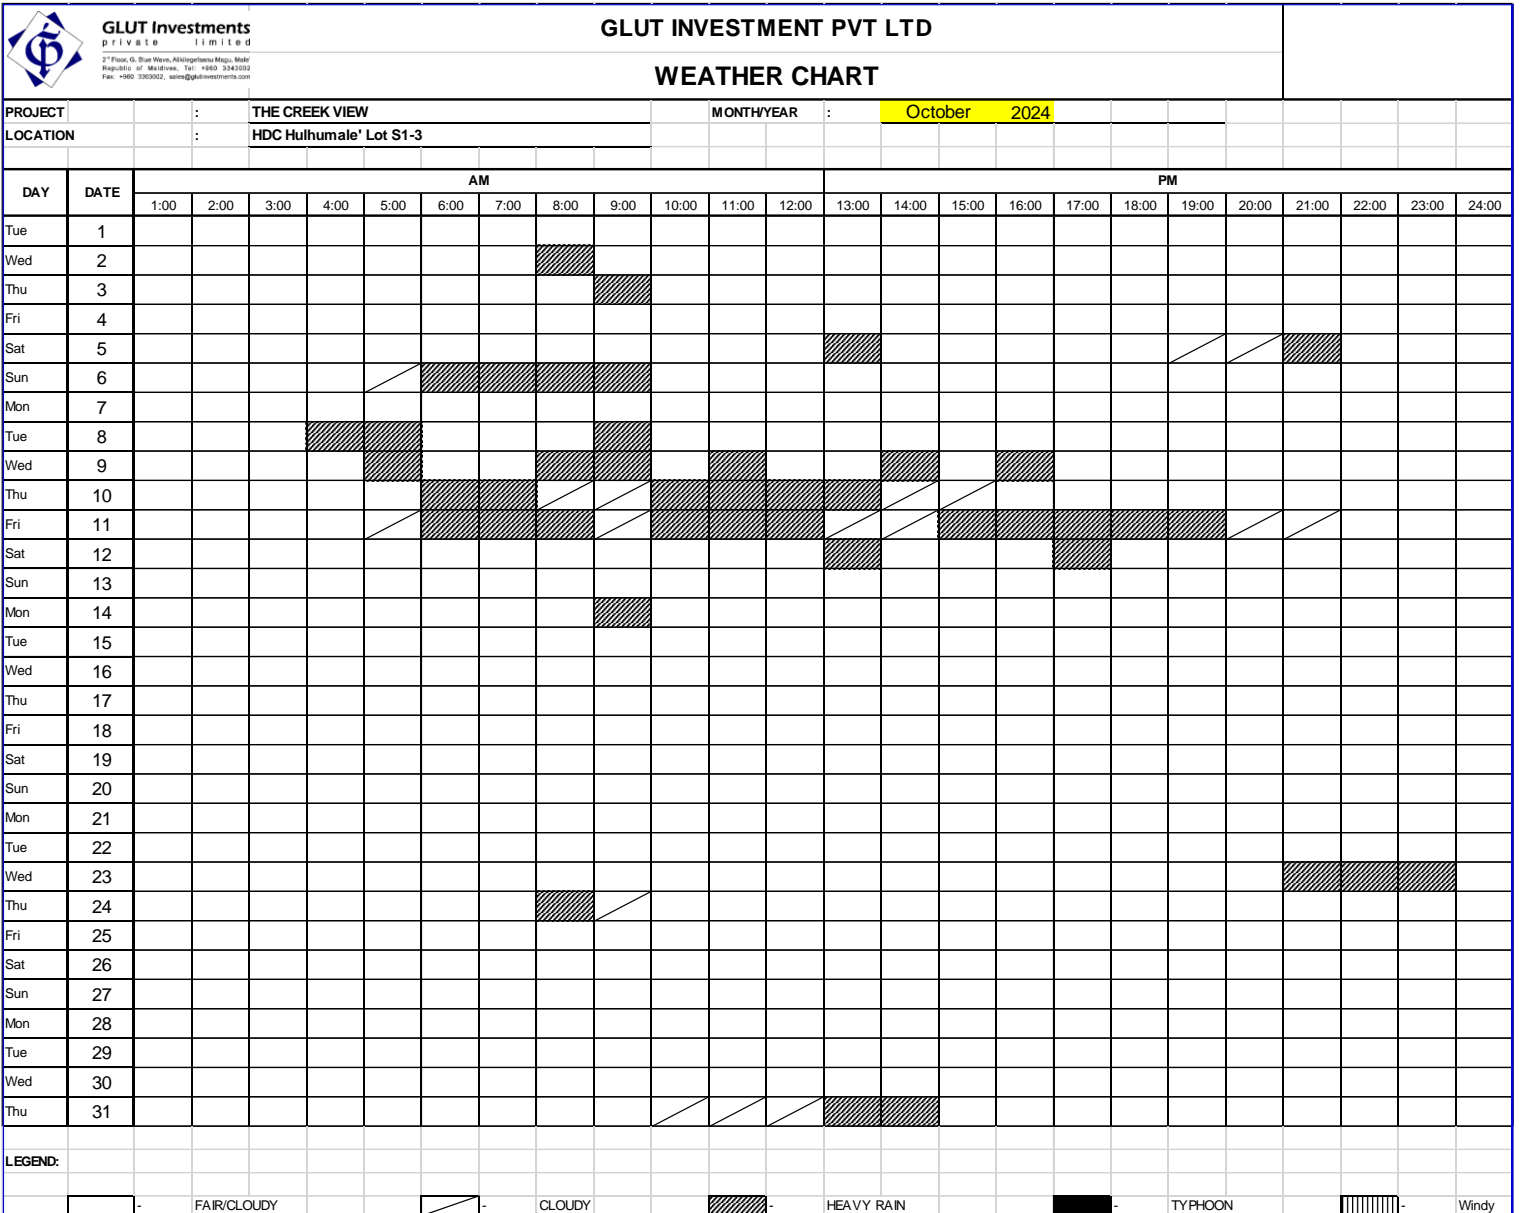

2022		
Months	Rainy Days	Days to Claim
April	11	11
May	19	19
June	16	16
July	19	19
August	14	14
September	14	14
October	17	17
November	11	11
December	16	16
2023		
January	7	7
February	1	1
March	9	9
April	10	10
May	10	10
June	13	13
July	9	9
August	12	12
September	12	12
October	20	20
November	20	20
December	19	19
2024		
January	5	5
February	8	8
March	4	4
April	8	8
May	20	20
June	9	9
July	16	16
August	16	16
September	16	16
October	13	13

10.0 SITE PROGRESS PHOTOS

10.1 October 2024 Site Photos



H and I Air well plastering



Roofing sheet laying



13th floor block work



Ground floor electrical room block work



13th floor internal plastering



11th floor tiling work



2nd to 13th floor ex painting work



Safety Net installation




Safety Net Installation




3rd floor primer and emulsion painting work





12th floor fresh water line

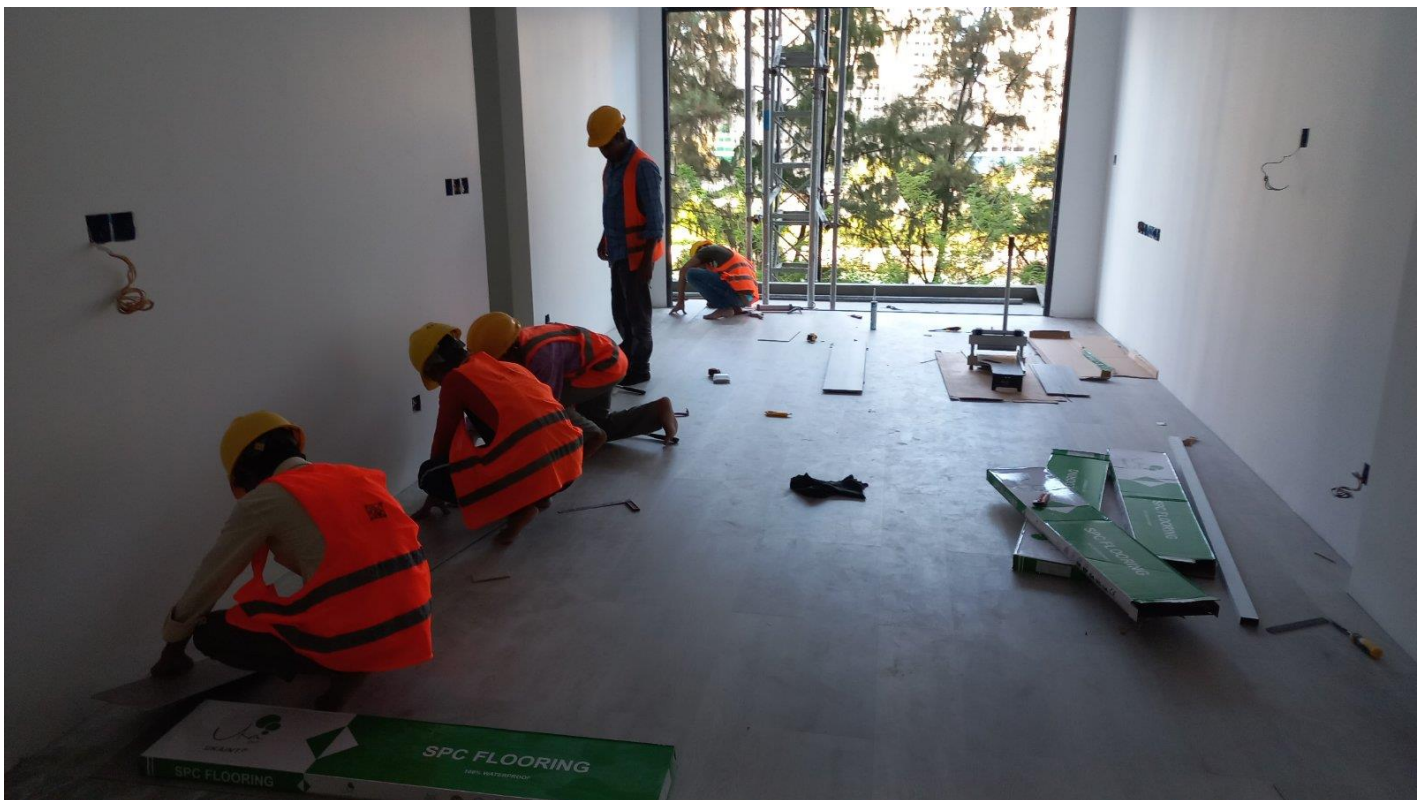

3rd floor SPC laying

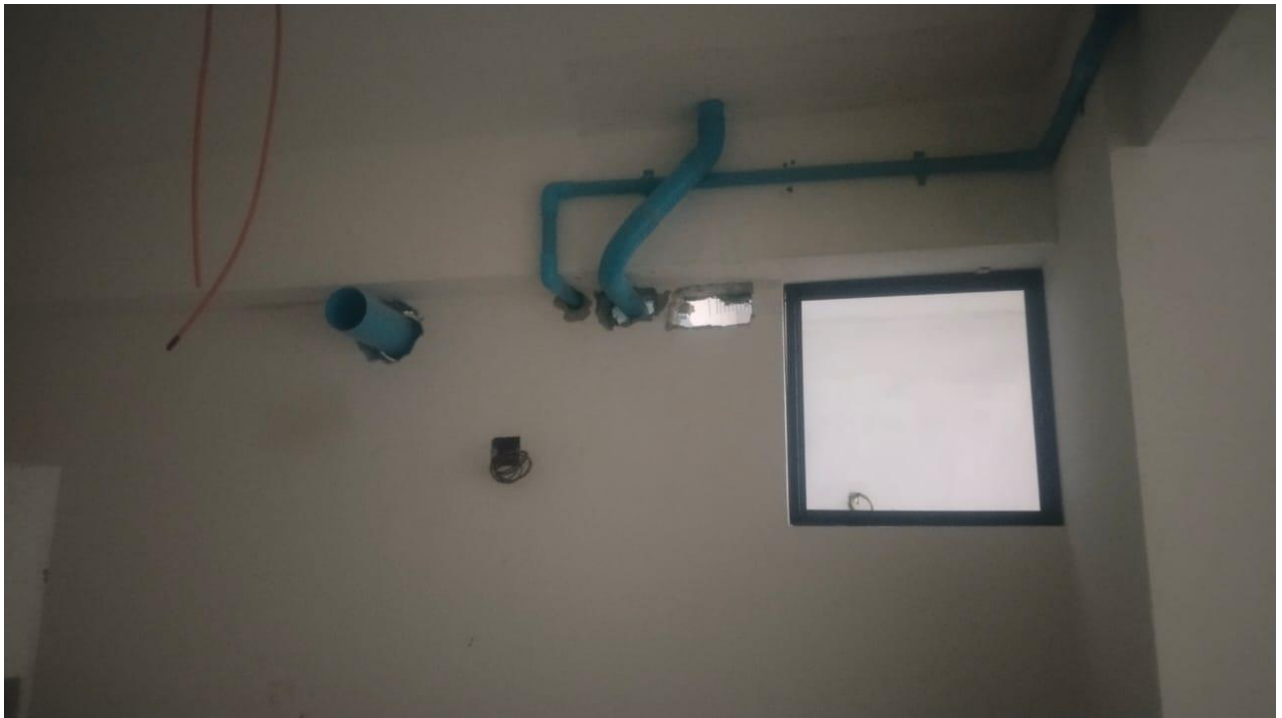

10th floor plumbing work

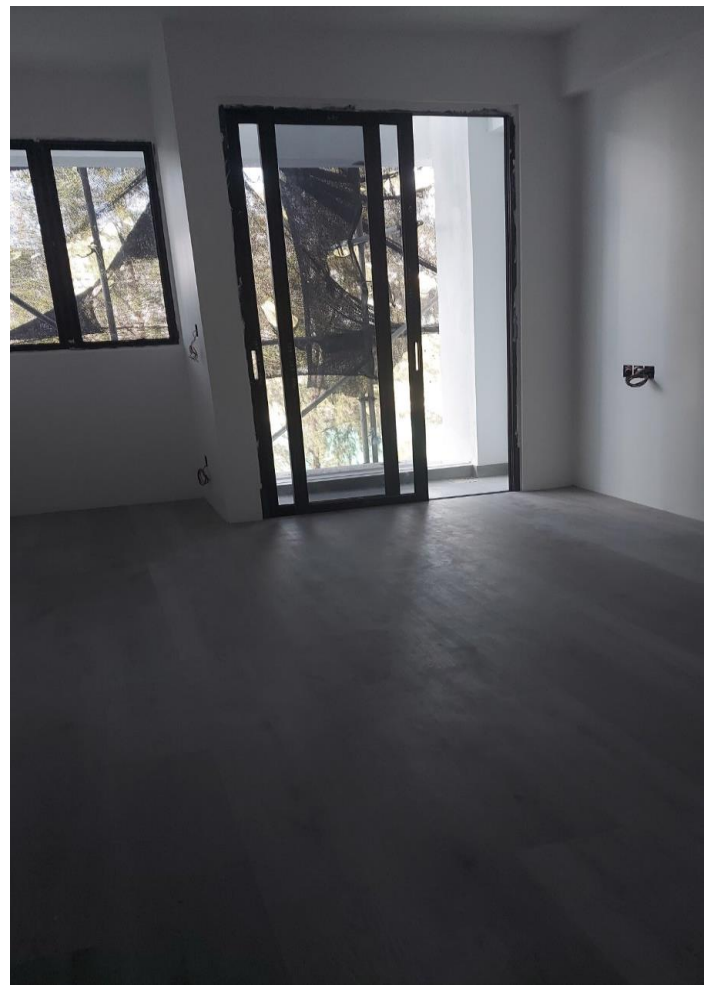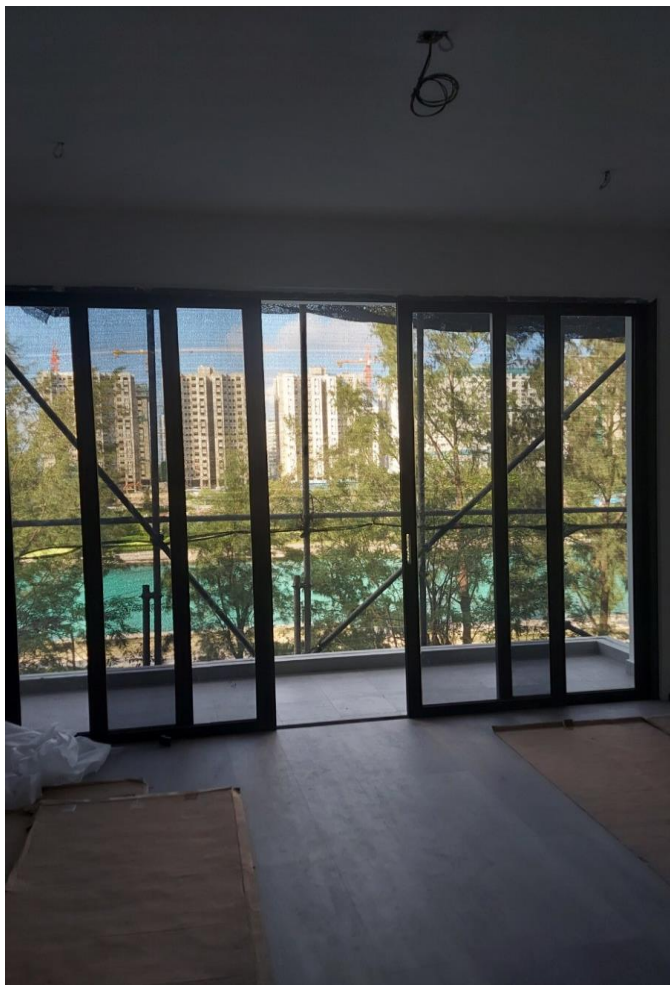

3rd floor Aluminium door fixing



3rd floor common area screeding



8th floor Apartment screeding




3rd floor WPC door fixing



3rd floor kitchen floor tile laying

PREPARED AND SUBMITTED BY GLUT INVESTMENTS PVT. LTD.

Prepared By:



Anandaraj
Civil Engineer (Glut)

Checked By:



Mohammed Shamin
Project Consultant
