

PROJECT PROGRESS REPORT

FEBRUARY 2024



DEVELOPER:



SAS e GLUT JV Pvt Ltd

CONTRACTOR:



GLUT Investments
private limited

PROJECT TITLE: MIXED USE RESIDENTIAL COMPLEX AT HULHUMALE (THE CREEK VIEW)
DEVELOPER: SASe GLUT JV PVT. LTD.
CONTRACTOR: GLUT INVESTMENTS PVT. LTD.
LOCATION: LOT NO: S1-3, LOT: 11445 HULHUMALE', MALDIVES

PROJECT BREIF:

The Creek View at Hulhumale Phase-1 is a pristine, spacious condominium project brought to you by the company SASe Glut Joint-venture Private Limited. The development is located at Lot 11445, Kuredhimaa Hingun overseeing the creek separating phase I and phase II of Hulhumale'.

The building comprises 114 apartments with 2 room, 3 room and 4 room units, each carefully designed to ensure the separation of spaces with special attention given to privacy and offer a homely feeling. Each apartment has a mini backyard with access from the kitchen. The kitchens are designed as enclosed spaces separated by masonry and glass partitions.

The apartment units are designed to make the most of natural air and light ventilation with floor to ceiling high windows. These large windows are also placed with an offset from the periphery to prevent direct sun and rain exposure. As many prefer to shape every element of their home environment, carefully choosing their furniture, curtain & paint, we find it best to engage prospective tenants during the interior design process. Those looking to occupy the new home hassle-free have the option to choose from fully fitted, furnished units that come in a different configuration of colour, style & décor.

The access to the residential units is well separated from the commercial area on the ground and the first floor to ensure privacy and safety to tenants. In addition, the entrance lobby is designed with a waiting & meeting area for visitors, limiting visitors' access to apartment floors.

Parking is arranged at the basement, ground and first floor with the basement exclusively for car parking. Amenities such as the pool and playgrounds are at ground level. At the same time, all utility services are located at the service lobby to avoid direct contact with any service team member. A separate service elevator will be allocated for the use of the service team for transporting furniture items and trash bins.

1.0 PROJECT PROGRESS REPORT BREIF

- 1.1 All permits and project documentation requirements are submitted and process accordingly.
- 1.2 Drawings and details are submitted and approved.
- 1.3 All land concern and preparation are addressed in coordinated according to the local government requirements.
- 1.4 All necessary activities and preparation are in progress.

2.0 CURRENT STATUS

2.1 Materials and Equipment's Procurement

2.1.1 Material and Equipment Received

- 2.1.1.1 Cement, Sand, Aggregates, Pipes, Blocks, Tiles, Putty, Paint and Wire

2.2 Project Progress Meeting by Urbanco

- 2.2.1 Date: 14th February 24

2.3 Site Coordination Meeting with Consultants

- 2.3.1 Date: 18th February 24 and 29th February 24

2.4 Site Coordination Meeting with Sase – Glut

- 2.4.1 Date: 28th February 24 and 29th February 24

2.5 Issue for Construction Drawing

2.5.1 Structural drawings

- 2.5.1.1 Structural Floor Plans – Partial Received

2.5.2 Architectural drawings

- 2.5.2.1 Architectural Floor Plans – Partial Received


2.5.3 Electrical drawings

- 2.5.3.1 Electrical Floor Plans – Partial Received

2.5.4 Electrical drawings

- 2.5.4.1 Plumbing Floor Plans – Partial Received

2.6 Project Status

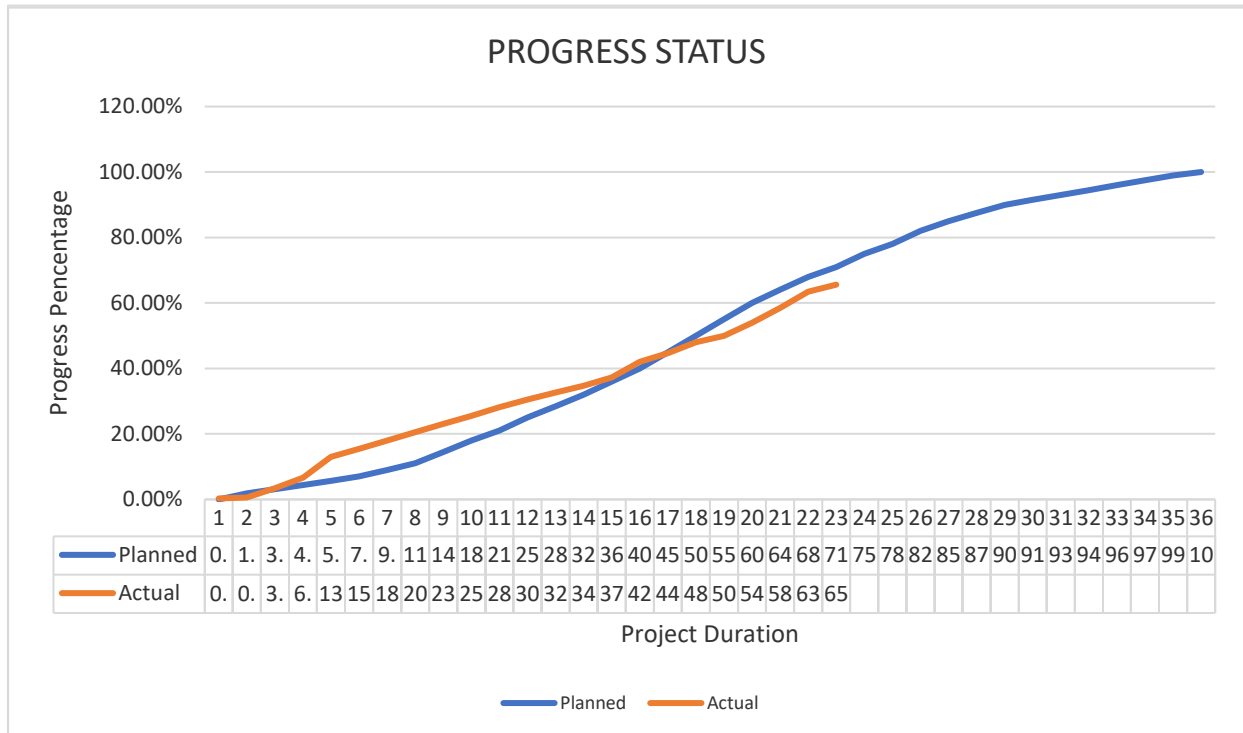

3.0 ONGOING/COMPLETED WORKS

- 3.1 12th floor block work and plastering almost completed
- 3.2 Putty work completed up to 8th floor
- 3.3 Right side elevation E5,6,12th to 2nd floor ex plastering completed
- 3.4 Right side Elevation E7,8 12th to 2nd floor ex plastering completed
- 3.5 Type H and I air well external plastering completed 11th to 3rd
- 3.6 Left elevation E7,8 upto 3th floor and E5,6 12th floor completed
- 3.7 Safety net installation and scaffolding internal perimeter
- 3.8 2nd floor passage fresh water line plumbing work completed
- 3.9 Socket fixing 9th floor and wiring work 5th floor completed

4.0 UPCOMING WORKS FOR NEXT MONTH

- 4.1 Left elevation E5,6,7,8 ex plastering
- 4.2 13th floor wall kickers and block work will start
- 4.3 Left and right elevation plastering will start
- 4.4 EFG air well external plastering complete
- 4.5 Socket will fix 12th floor, wiring will complete 8th floor
- 4.6 Plumbing work 4,5,6 floor will complete
- 4.7 3rd floor toilet and wall tile work complete
- 4.8 Water proofing 4,5,6th floor complete
- 4.9 Safety net installation and internal perimeter scaffolding installation

5.0 ACCIDENT REPORT

5.1 No accident was reported

6.0 CHALLENGES FACED DURING CONSTRUCTION / IMPLEMENTATION

6.1 Weather disruption due to heavy wind and rain (see weather chart–9.0)

7.0 INSTRUCTION GIVEN ON SITE


7.1 Minutes of meeting dated: 1Feb 2024, 8 Feb 2024,15 Feb 2024, 22 Feb 2024 and 29 Feb 2024.

8.0 DOCUMENTATION OF APPROVED MATERIALS

8.1 Cube Test Report
8.1.1 No report

9.0 WEATHER CHART

9.1 February 2024

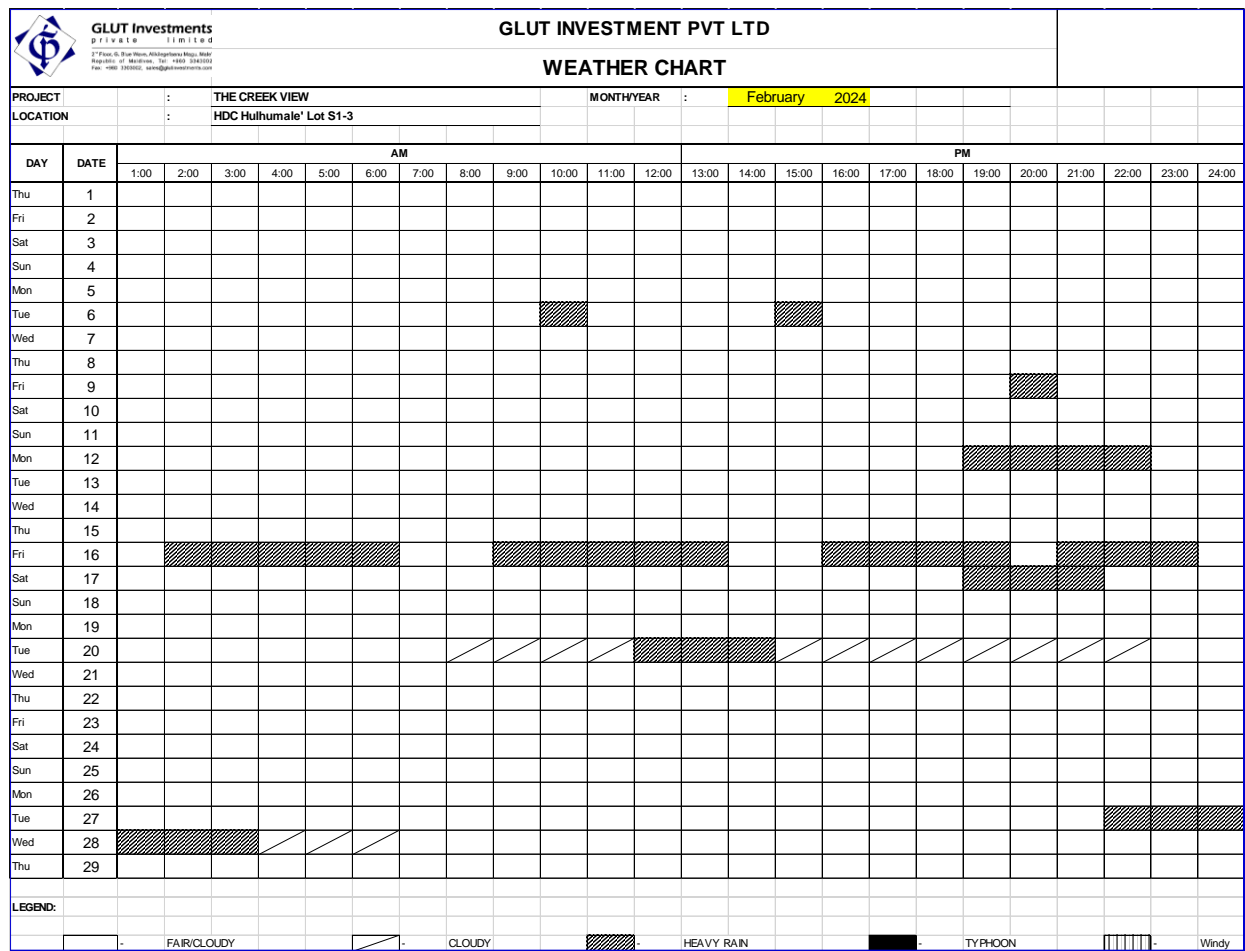


2022		
Months	Rainy Days	Days to Claim
March	5	5
April	11	11
May	19	19
June	16	16
July	19	19
August	14	14
September	14	14
October	17	17
November	11	11
December	16	16
2023		
January	7	7
February	1	1
March	9	9
April	10	10
May	10	10
June	13	13
July	9	9
August	12	12
September	12	12
October	20	20
November	20	20
December	19	19
2024		
January	5	5
February	8	8

10.0 SITE PROGRESS PHOTO


10.1 February 2024 Site Photos




Elevation E5,E6 external plastering

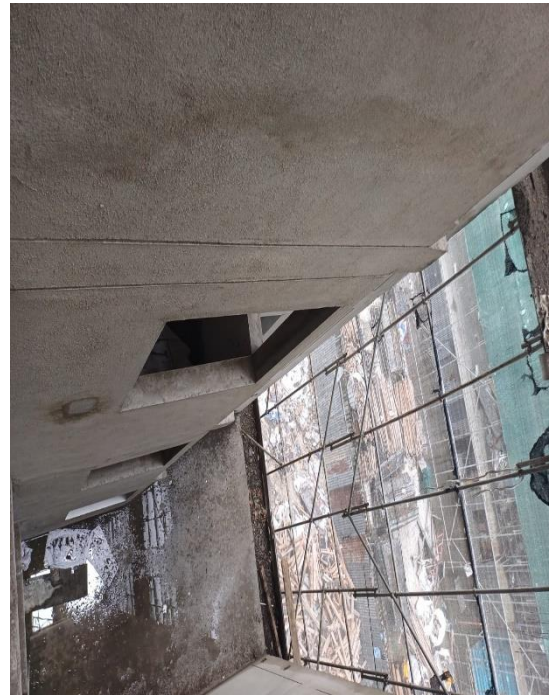

Elevation E7,E8 external plastering

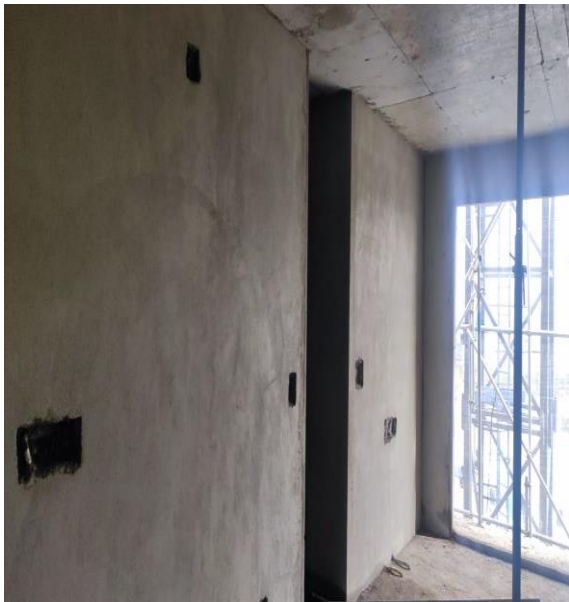

12th floor plastering work continuous

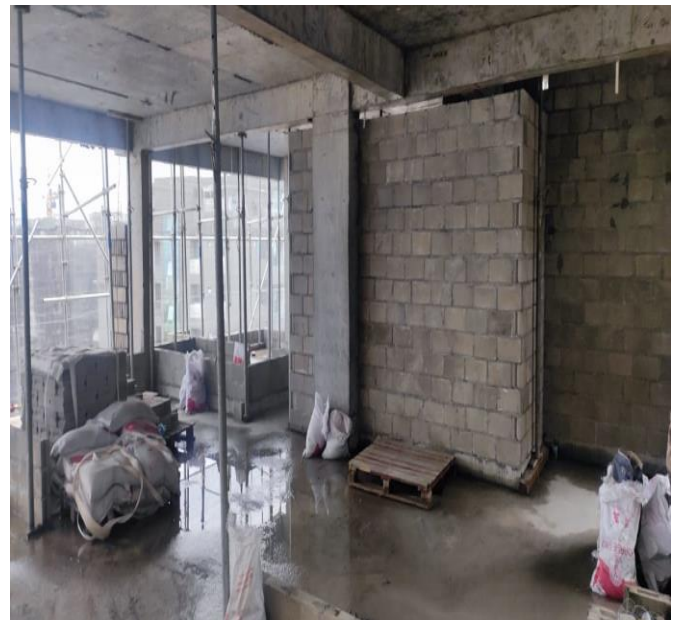


12th floor block work continue



8th floor socket box fixing



4th floor plumbing work continues

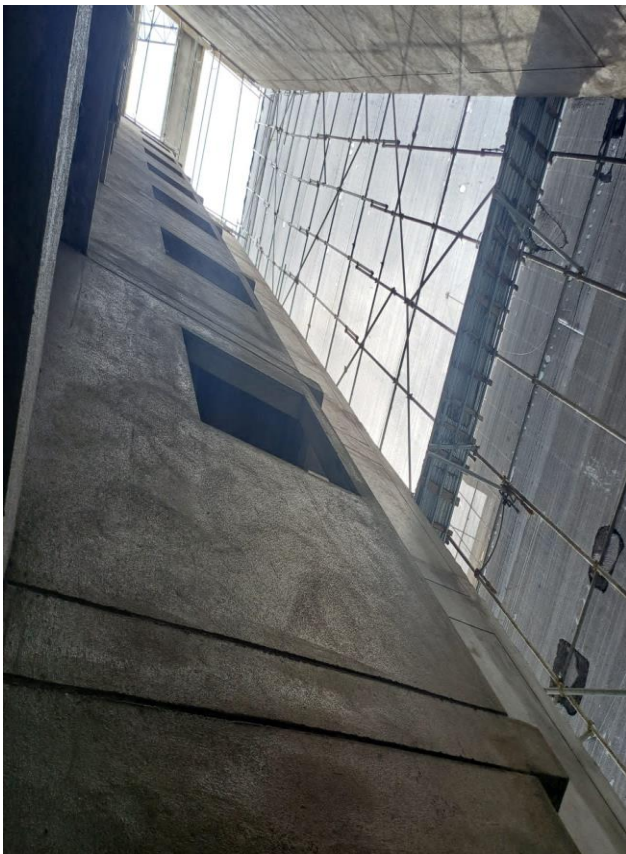

Left side E5 6 ex plastering work



3rd floor fresh water line




Safety Net installation



Safety Net Installation



3rd floor tile work

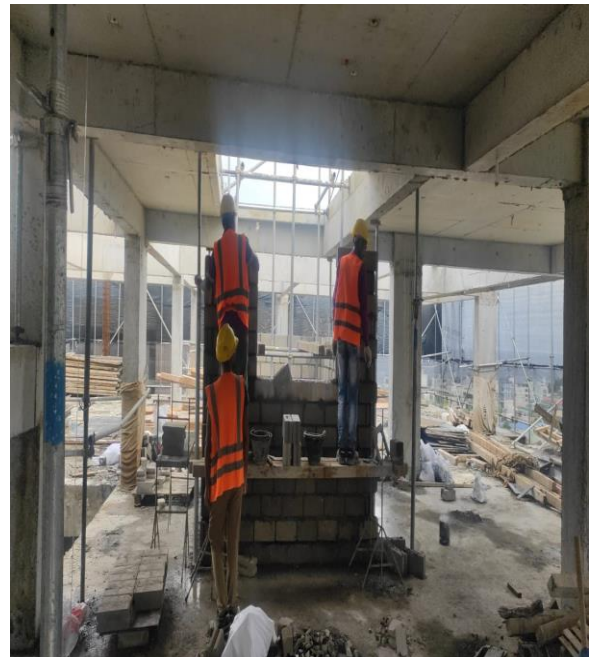

13th floor block work



Common area wall kicker



4th floor toilet plumbing work




8th floor wall and ceiling putty work



9th floor wall and ceiling putty work

PREPARED AND SUBMITTED BY GLUT INVESTMENTS PVT. LTD.

Prepared By:



Anandaraj
Civil Engineer (Glut)

Checked By:

Mohammed Shamin
Project Consultant
